


工程表

工事名: 立川基地跡地昭島地区国営公園南線外道路その他工事他3件

鴻池・岩倉建設工事共同企業体

種別	細別	平成27年 8月																															備考
		1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	
		土	日	月	火	水	木	金	土	日	月	火	水	木	金	土	日	月	火	水	木	金	土	日	月	火	水	木	金	土	日	月	
《北工区③区域》 準備工	進入路設置工事	●	●	●				●																									
	伐採工事	●	●	●				●	●	●																							
備考																																	

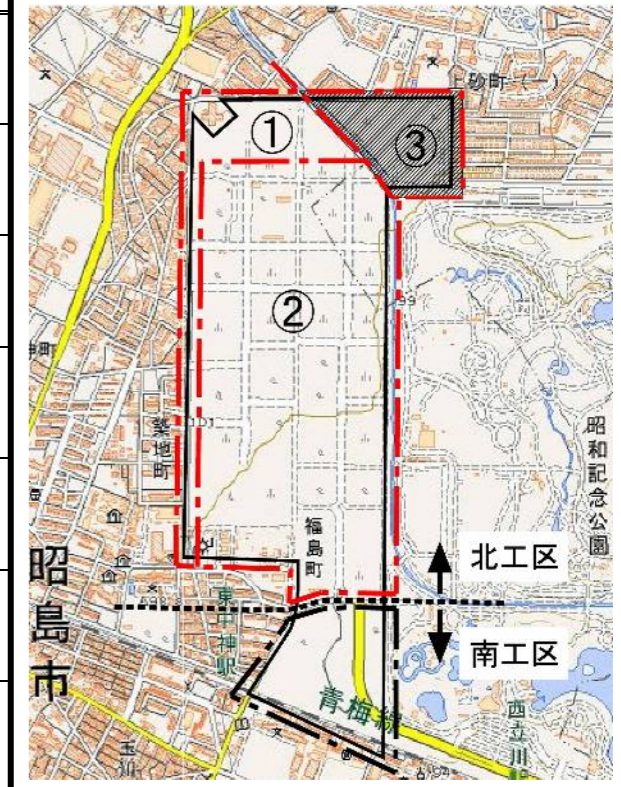


7月25日 時点
進捗状況

除草完了



進入路設置箇所

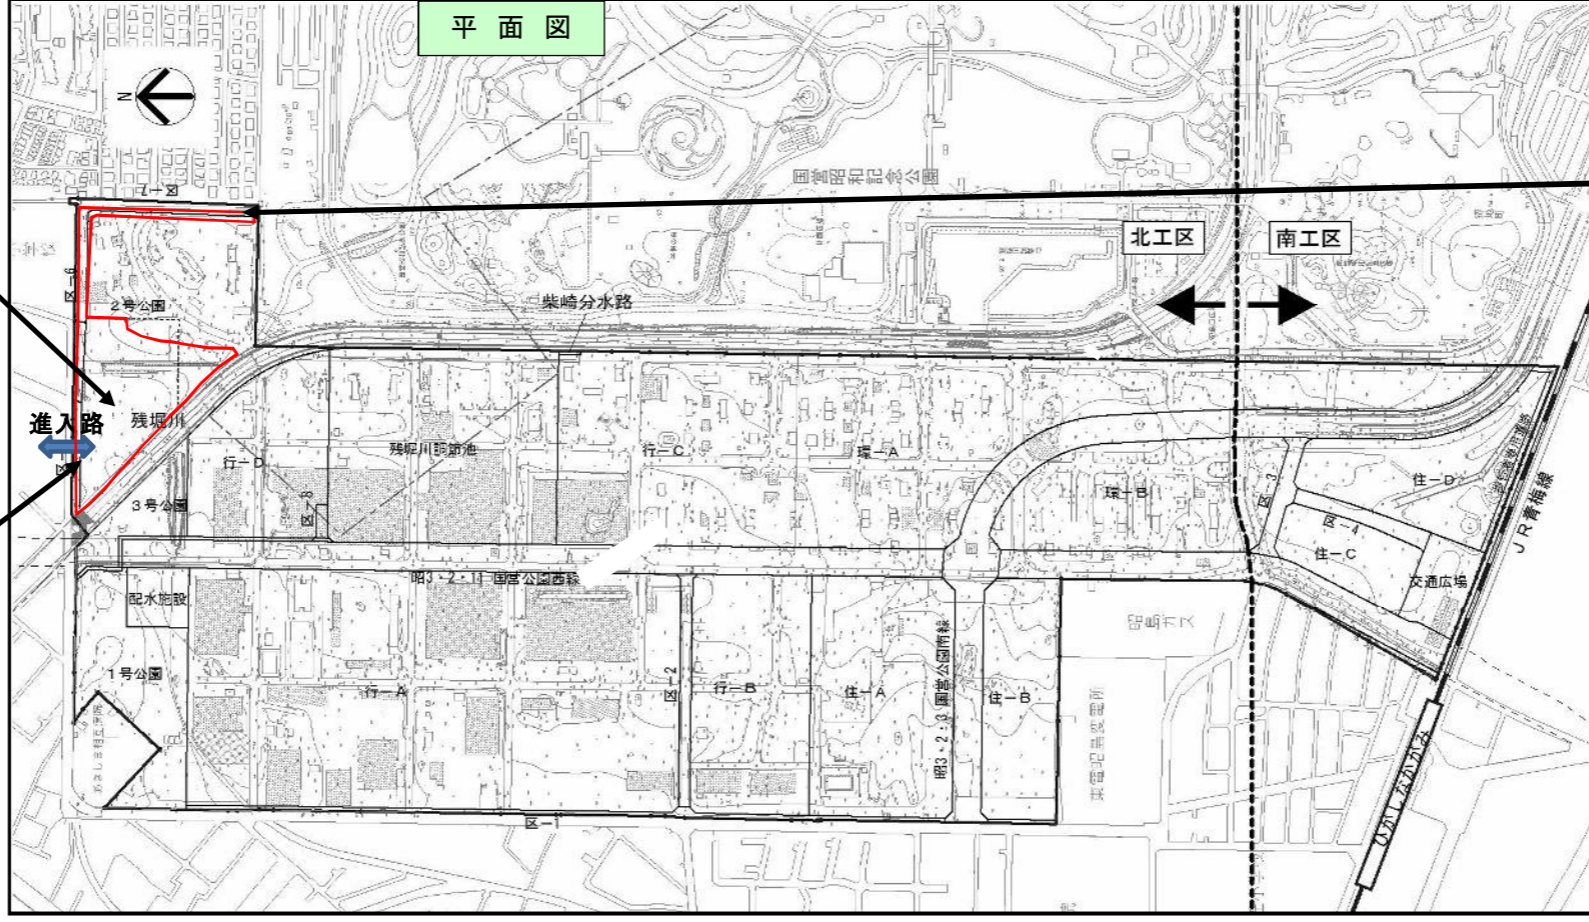

現況

